GlobalTech: Building Accessible Support Systems for All Employees

Simulated brief: a fictional global employer moving its staff onto self-service. Not a client engagement.

Vedant Audichya · May to July 2026
Project and team lead, 6-person team
Simulated brief · MSc Business Analysis and Consulting

THE QUESTION

Four support pages breach WCAG, carry a Red urgent audit rating and have already generated HR reports of employee stress. What should be fixed first, and is fixing it worth funding?

1 It fails as a service before it fails as a compliance obligation

Reframing the brief changed what the analysis had to prove. Inaccessible design pushes work back onto managers, HR and the service desk across 561,005 annual views, so the case was built on productivity, support deflection and retention rather than on legal exposure alone.

2 The sequence is defensible, not just asserted

A transparent MCDA scored four pages on traffic, defect count, process criticality, legal and HR sensitivity, and feasibility. Training and Learning ranked first at 88, HR Portal second at 82.7. A 1,000-iteration stress test on weights and scores held the top two in over 95% of re-runs.

3 The money case clears comfortably and states its own weakness

Base case: £306,273 implementation cost, £485,404 annual gross benefit, £787,496 three-year NPV, benefit-cost ratio 2.38. I built the financial model, including the Monte Carlo and the scenario layer.


4 The winning argument was about who owns it afterwards

The recommendation is an eight-month sequenced programme with WCAG 2.2 AA as a release gate, named product ownership and accessibility regression testing, rather than a page-by-page cosmetic clean-up that would decay within a release cycle.


LIMITATIONS, AND WHAT WOULD CHANGE THE ANSWER

These are decision-support estimates, not audited figures. The largest benefit lines rest on assumptions the workbook exposes rather than hides: affected visit share, avoidable delay per visit, improvement capture rate and prevented exits are all model assumptions flagged for validation during discovery, not measured values. The workbook publishes every input with its low, base and high range, source type and audit note precisely so GlobalTech can challenge or replace them. Page-view figures come from the client brief rather than from analytics exports.

The case survives its own uncertainty: 1,000 Monte Carlo runs

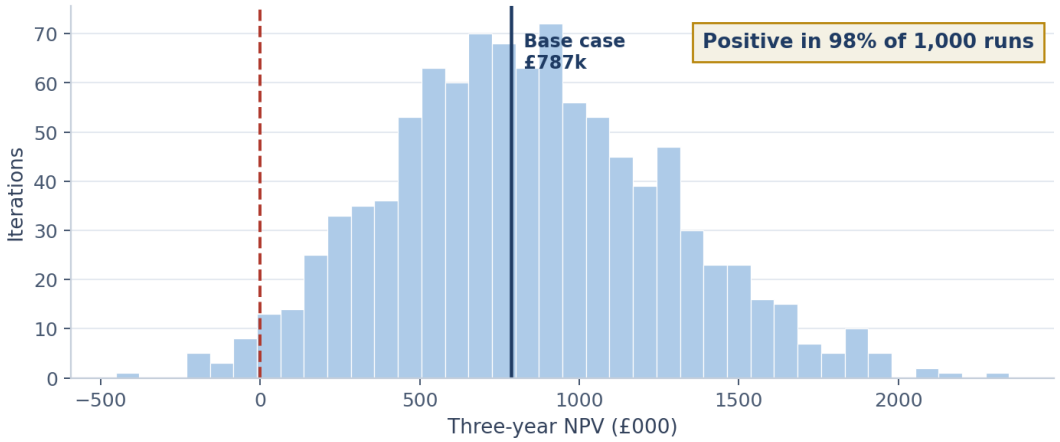

Every scenario stays positive, but the spread is 2.9x

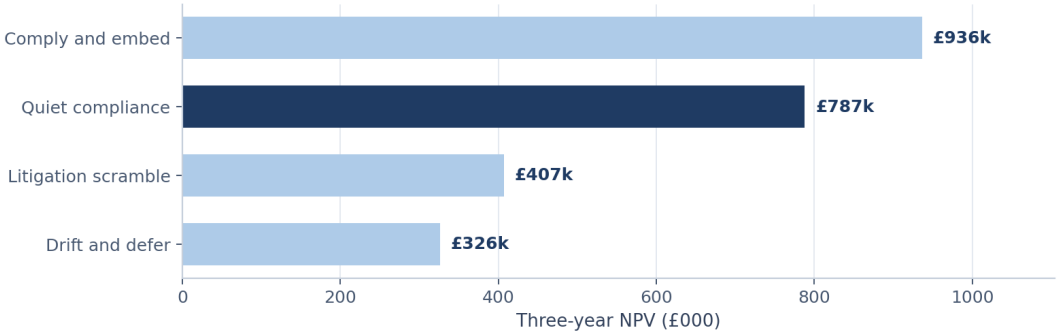

Built with Excel (MCDA, Monte Carlo, cost-benefit, scenario) · WCAG 2.2 AA audit · stakeholder typology

Delivered prioritised backlog · financial model · test strategy · 8-month roadmap
